




Tree No.	Species	D.B.H (cm)	Ownership	Condition of tree	Client's reason for removal	Arborist recommendation
1	Sugar maple	92	City	Tree health is fair, structure is poor. Decay present throughout, structure being supported by cables.	Remove due to structural concerns.	Remove, tree is not safe for retention.
2	Sugar maple	33	City	Tree health is good. Structure is fair.	Tree to be retained and protected.	CRZ fencing to be installed as per plan, installed at a 9ft radius. Closest excavation points are at a 10ft distance from trunk. During the demo phase work in the CRZ will be required to remove hardscape, arborist on-site during this to monitor, perform root pruning/dressing if required. Light backfill may also be required.
3	Norway maple	24	Private	Tree has been removed due to structural defects.		
4	Norway maple	44	Private	Health and structure are fair.	Remove conflict with construction.	Remove, tree falls within building foot print.
5	Norway maple	29	Private	Health is good, structure is fair, co-dominant stems.	Remove, tree is growing under fiber lines.	Remove, not a suitable species for location.
6	White spruce	21	Neighbours	Tree health is fair, sparse canopy.	Tree to be retained and protected.	CRZ fencing installed at 6ft from trunk, excavation will not impact tree.
7	White cedar	40	Neighbours	Tree health is fair. Structure is poor, splitting at co-dominant union.	Tree to be retained and protected.	CRZ fencing installed at 6ft from trunk, excavation will not impact tree.
<p>The following are measures to be implemented prior and during the construction process.</p> <ul style="list-style-type: none"> <li>-Critical root zone of retained trees must be protected as outlined above. Snow or metal fencing must be erected around the CRZ and signage should be installed to identify tree is being protected.</li> <li>-Pruning must be performed prior to construction to ensure tree limbs will not be in conflict with equipment and construction. Permission must be obtained to prune Municipal or neighbors trees. (performed by Certified Arborist).</li> <li>-No material or equipment is permitted within any CRZ.</li> <li>-No signs, notices or posters may be attached to the tree.</li> <li>-No grade changes within any CRZ.</li> <li>-Ensure exhaust fumes from equipment are not directed towards tree canopy's.</li> <li>-After excavation is complete exposed and damaged roots should be pruned (performed by Certified Arborist).</li> </ul> <p>Tree Planting recommendations,</p> <ul style="list-style-type: none"> <li>-New tree #1 &amp; 2, armstrong maple 50mm</li> <li>-New tree #3 &amp; 4, ivory silk lilac or serviceberry 50mm</li> </ul>						
<div style="display: flex; justify-content: space-around;">   </div>						
			Tree 1			Tree 2




Tree 4

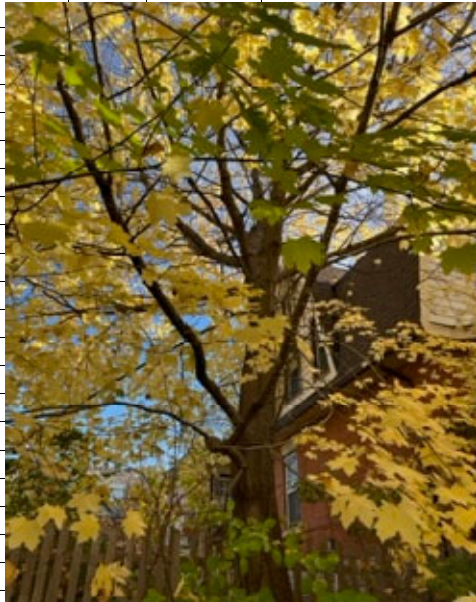


Tree 5



Tree 6

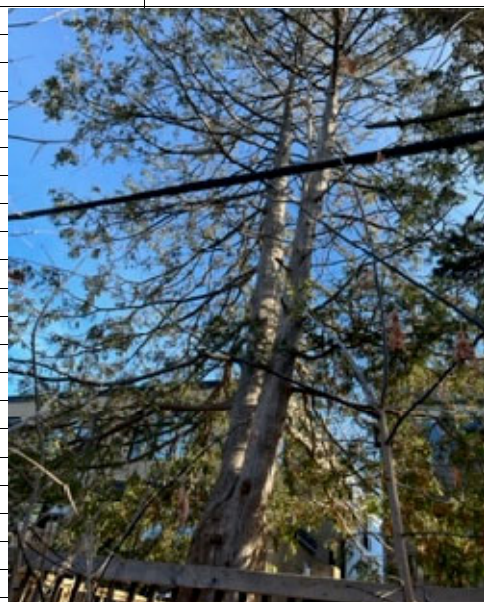

Tree 7

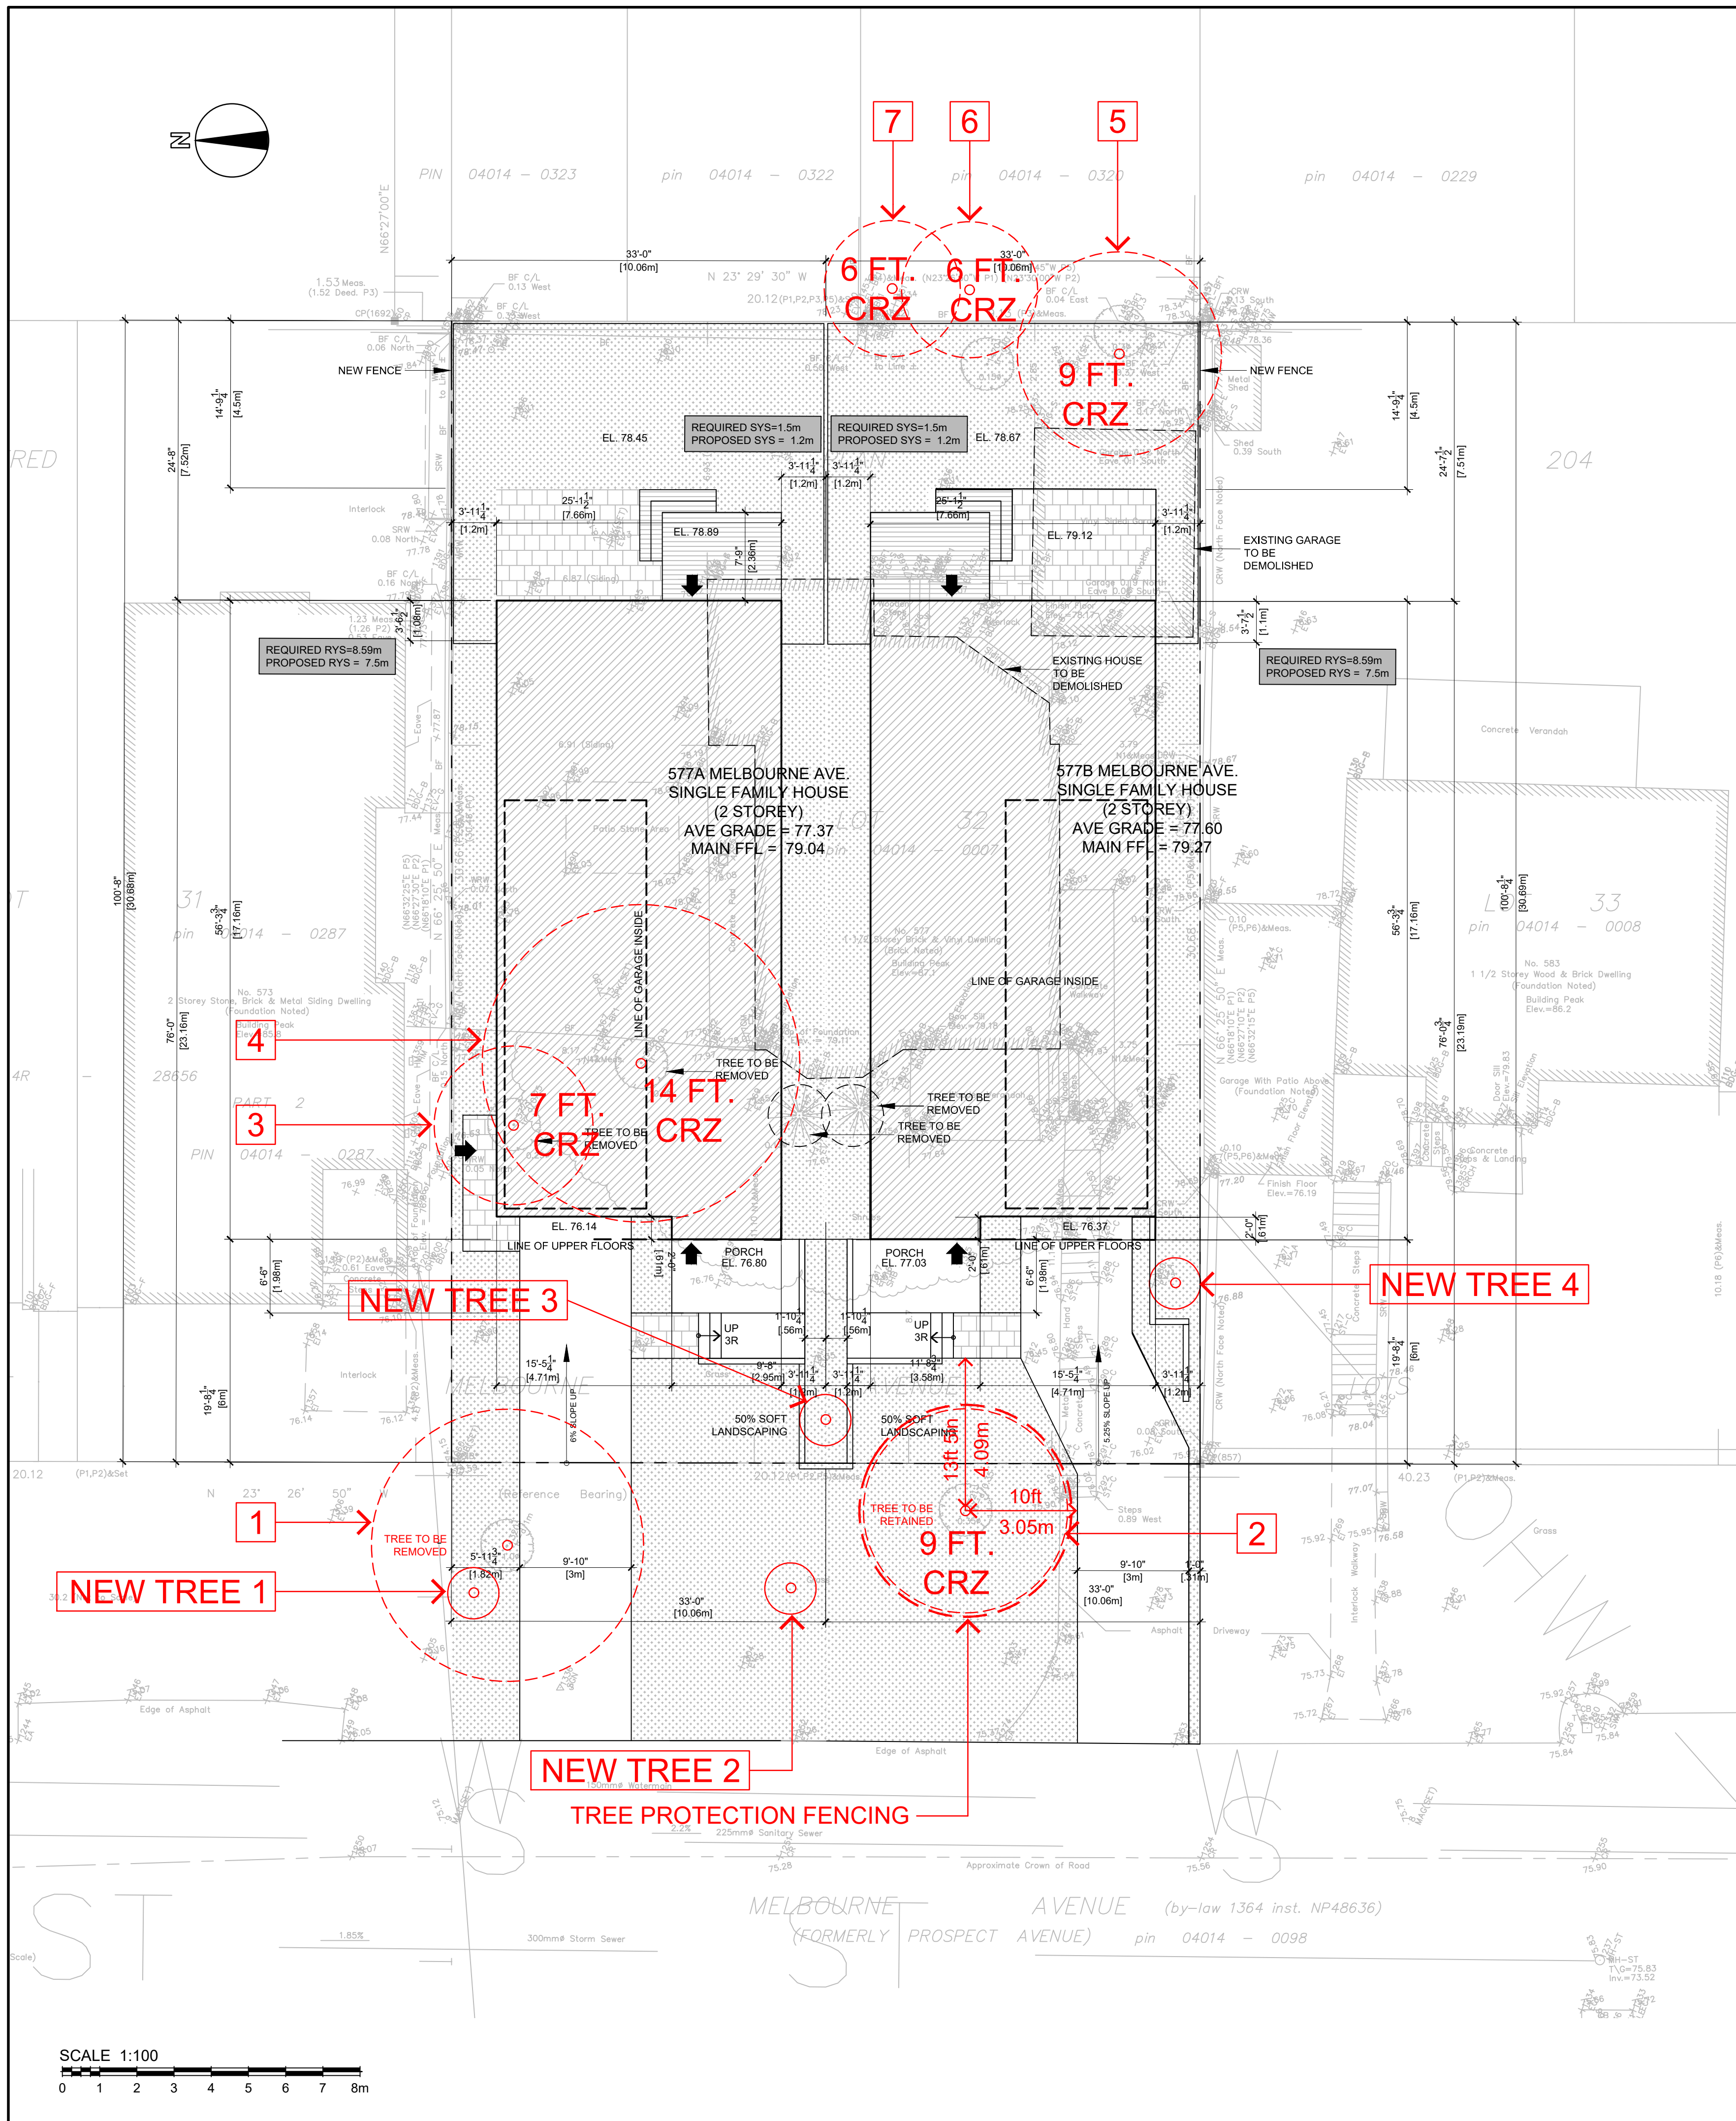

**NOTE:**  
 ARBORIST ON-SITE DURING  
 EXCAVATION NEAR CRZ'S. ANY  
 EXPOSED OR DAMAGED ROOT TO  
 BE PRUNED AND COVERED WITH  
 BURLAP UNTIL AREA IS  
 BACKFILLED.

577A MELBOURNE AVENUE  
 OTTAWA ONTARIO  
 TREE INFORMATION REPORT



REVISED NOVEMBER 15, 2023
